

WATER RESOURCES Management Update


Barnstable Town Council
August 2026

Prepared by:
Barnstable Department of Public Works




Fall 2026 Sewer Construction: What to Expect

Roadwork resumes after Labor Day, with active construction concentrated in Centerville, Marstons Mills, and Osterville.

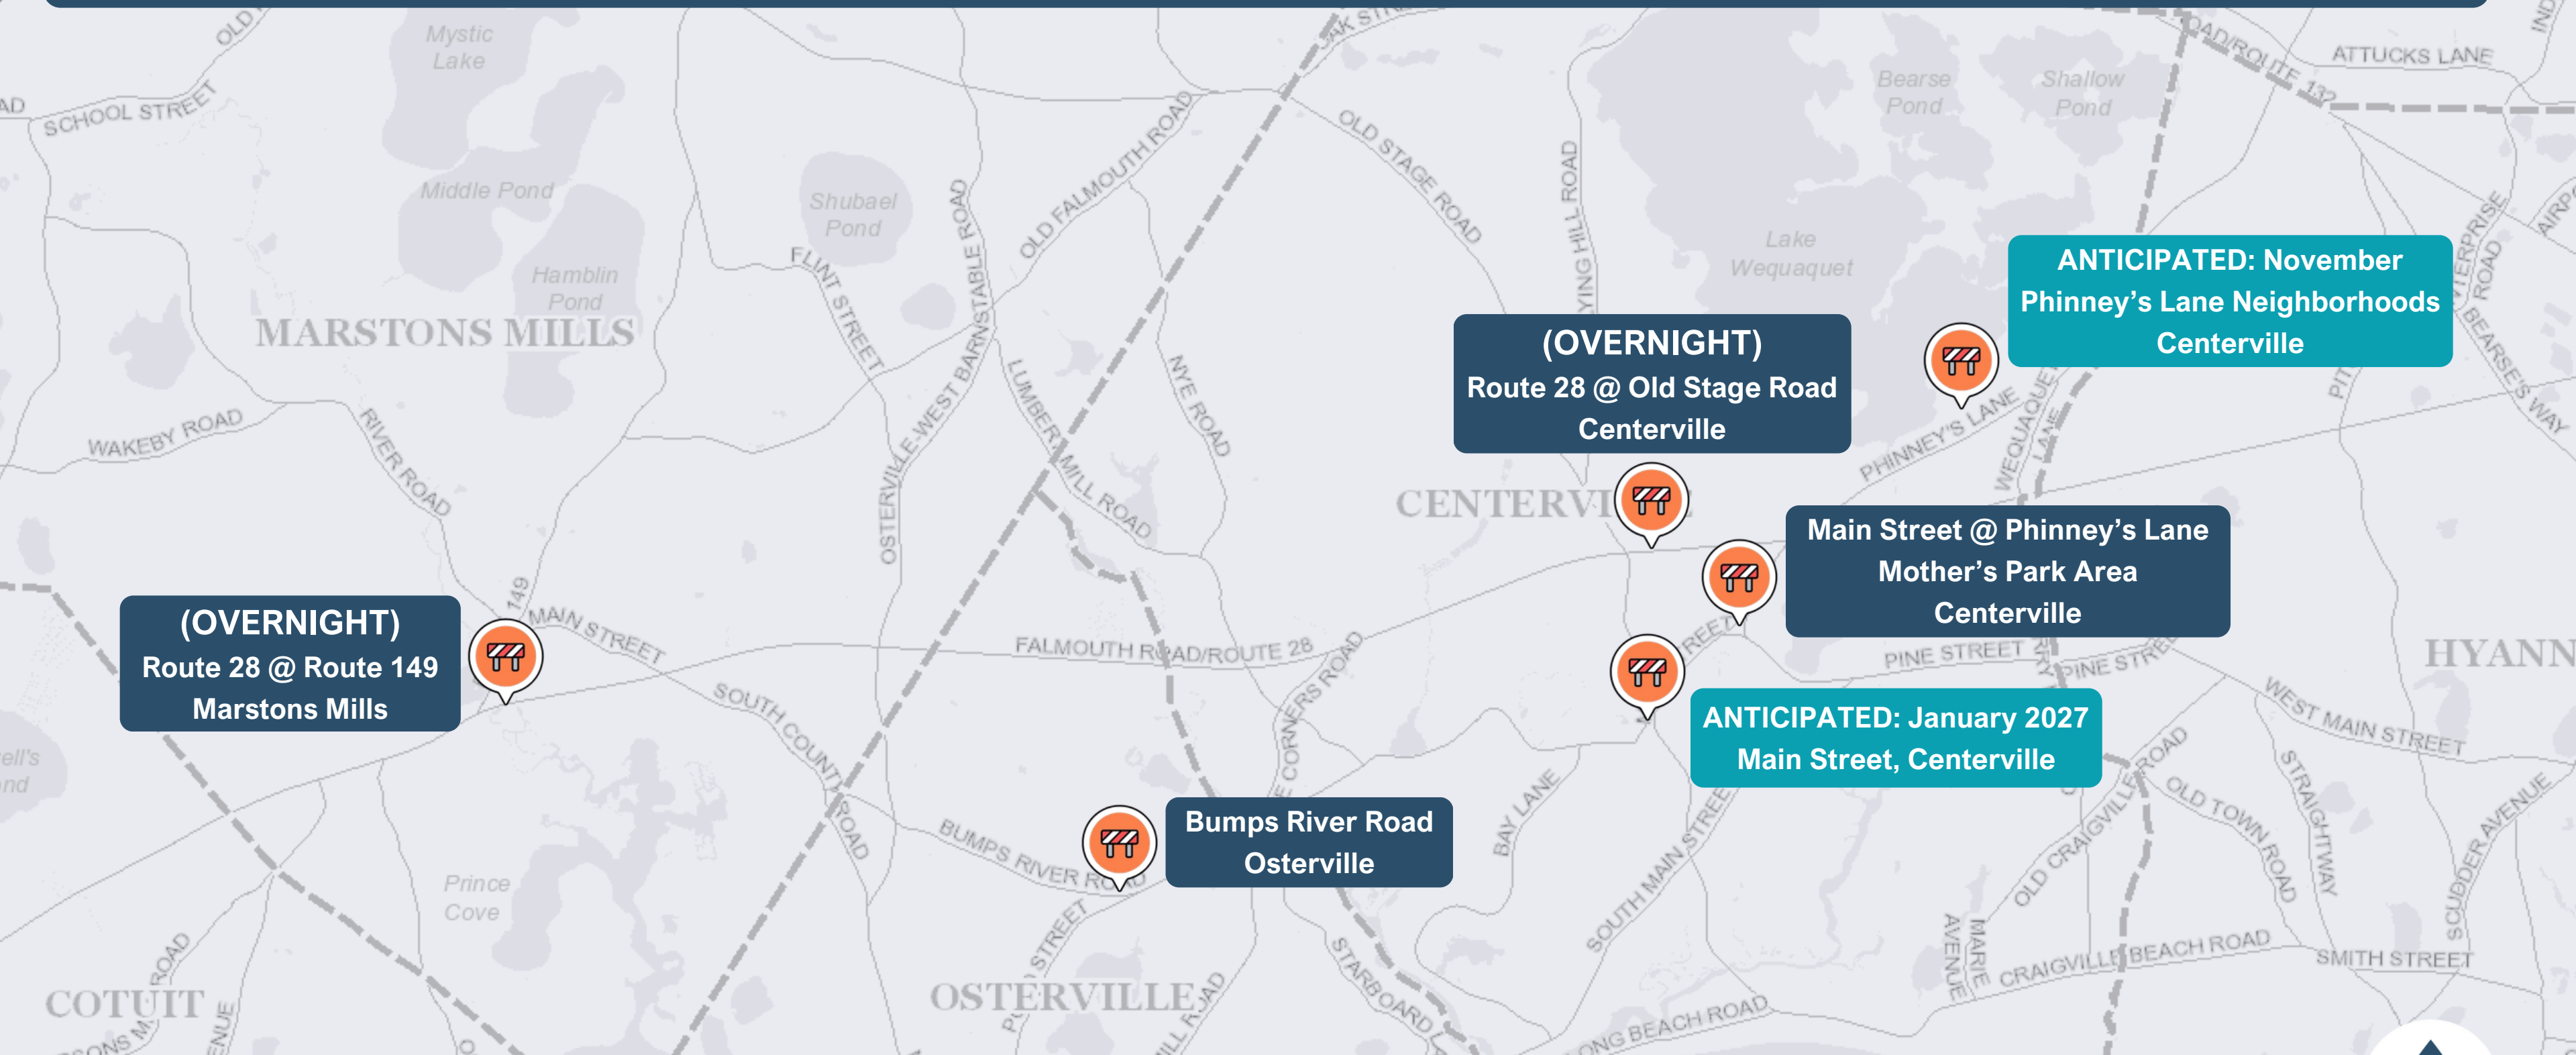

Anticipated Fall 2026 Schedule

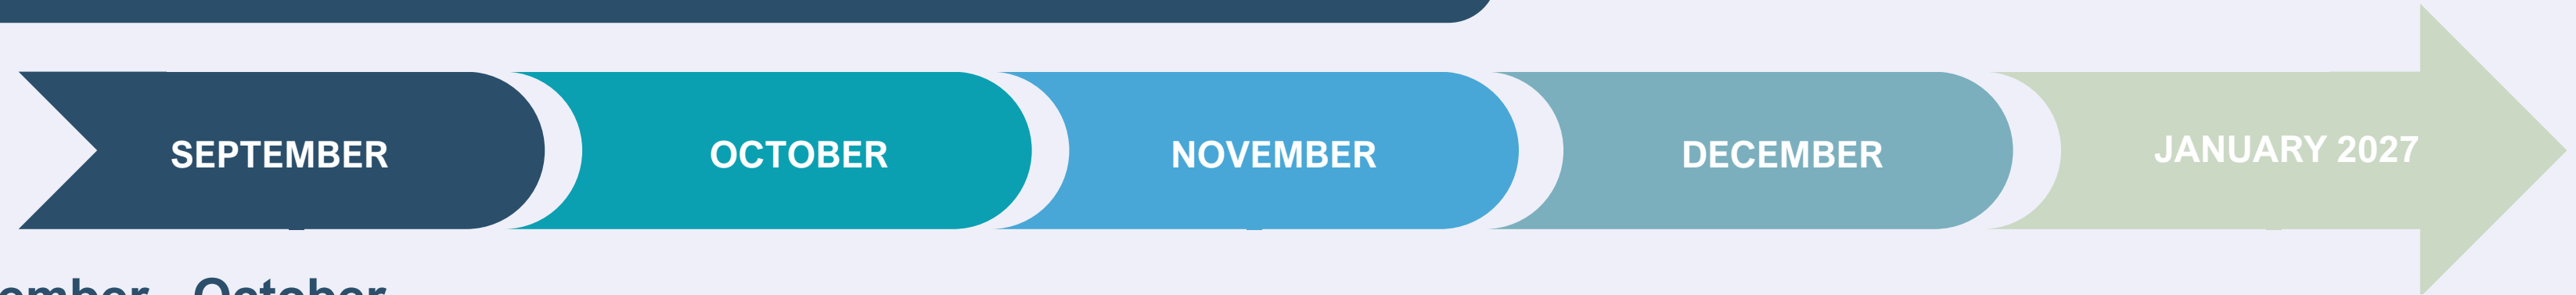

September - October

- **Route 28 — 2 locations in Centerville and Marstons Mills**
 - Centerville: Approximately 1661 Falmouth Road, advancing toward intersection of Route 28 @ Old Stage Road
 - Marstons Mills: Intersection of Route 149, advancing along Route 28 toward Centerville
 - All work performed OVERNIGHT from 7:00 PM to 6:00 AM
- **Main Street, Centerville – Area of Mother’s Park**
 - Crews will resume work at intersection of Main Street and Phinney’s Lane, advancing toward intersection of Main Street @ Old Stage Road
- **Bumps River Road, Osterville**
 - Crews will resume construction on Bumps River Road, advancing toward Osterville-West Barnstable Road


November - January

- **Phinney’s Lane neighborhoods**
 - Anticipated to begin in November
 - Crews will perform construction neighborhood-by-neighborhood; schedule in development
- **Main Street, Centerville**
 - Anticipated to begin in January 2027
 - Schedule in development

Construction will move throughout the season. Work zones and traffic impacts will change as projects progress.



Route 28 West Sewer Expansion Project

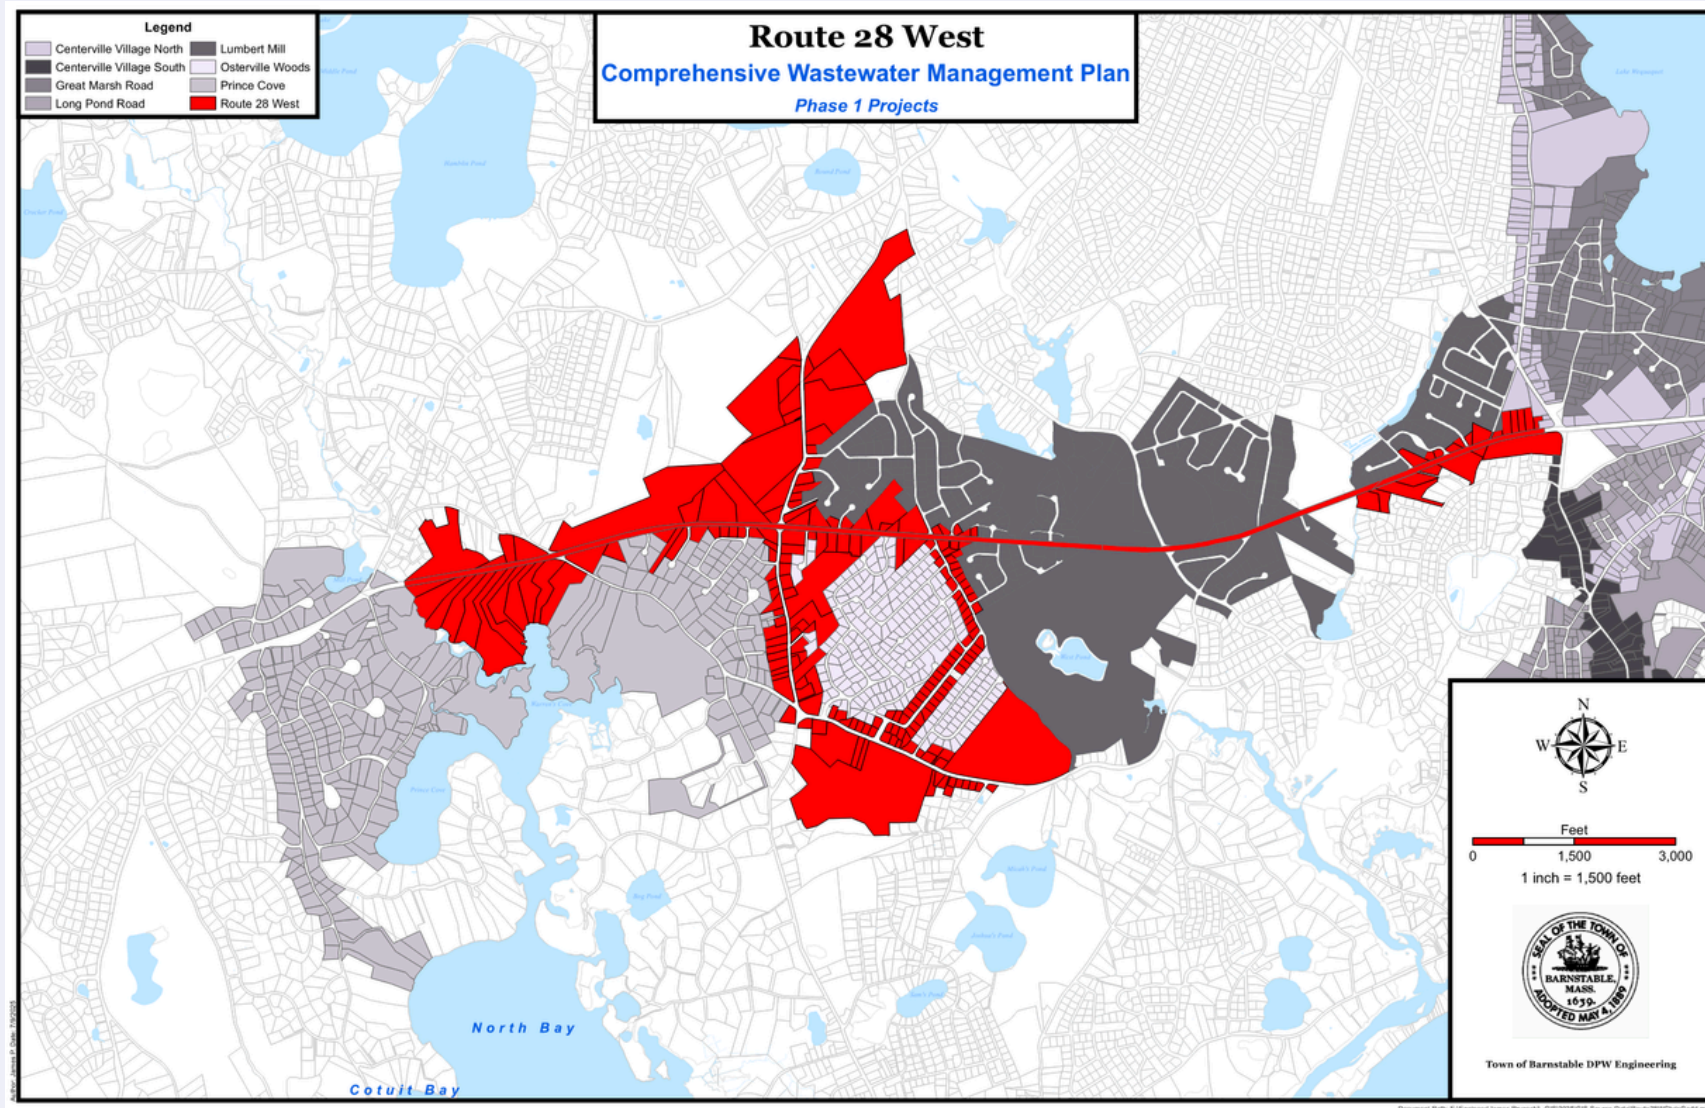

Summer Work Continues on Local Roads

Contractor currently working on Oldham Road, Osterville

- Crews installing force main from 181 Oldham Road (pump station site) toward Marion Way

Fall 2026 Construction Season

Work Zone 1 – Bumps River Road

- **WHEN:** September 8
- **TIME:** Monday - Friday, 7:00 AM to 5:00 PM
- **WHERE:** Work will begin within the vicinity of Marion Way advancing toward Osterville-West Barnstable Road
- **TRAFFIC IMPACT:** Road closure on Bumps River Road, from Osterville-West Barnstable Road to Pond Street


Work Zone 2 – Route 28 **(OVERNIGHT)**

- **WHEN:** September 14
- **TIME:** Overnight, Sunday - Thursday evenings, from 7:00 PM to 6:00 AM
- **WHERE:** Work will begin within the vicinity of the Marstons Mills Pump Station (former Marstons Mills School property, 2095 Main Street) advancing along Route 28 toward Centerville
- **TRAFFIC IMPACT:** A portion of Route 28 will be closed, from Route 149 to Osterville-West Barnstable Road




Route 28 West Sewer Expansion Project

Bumps River Road Traffic Management Plan

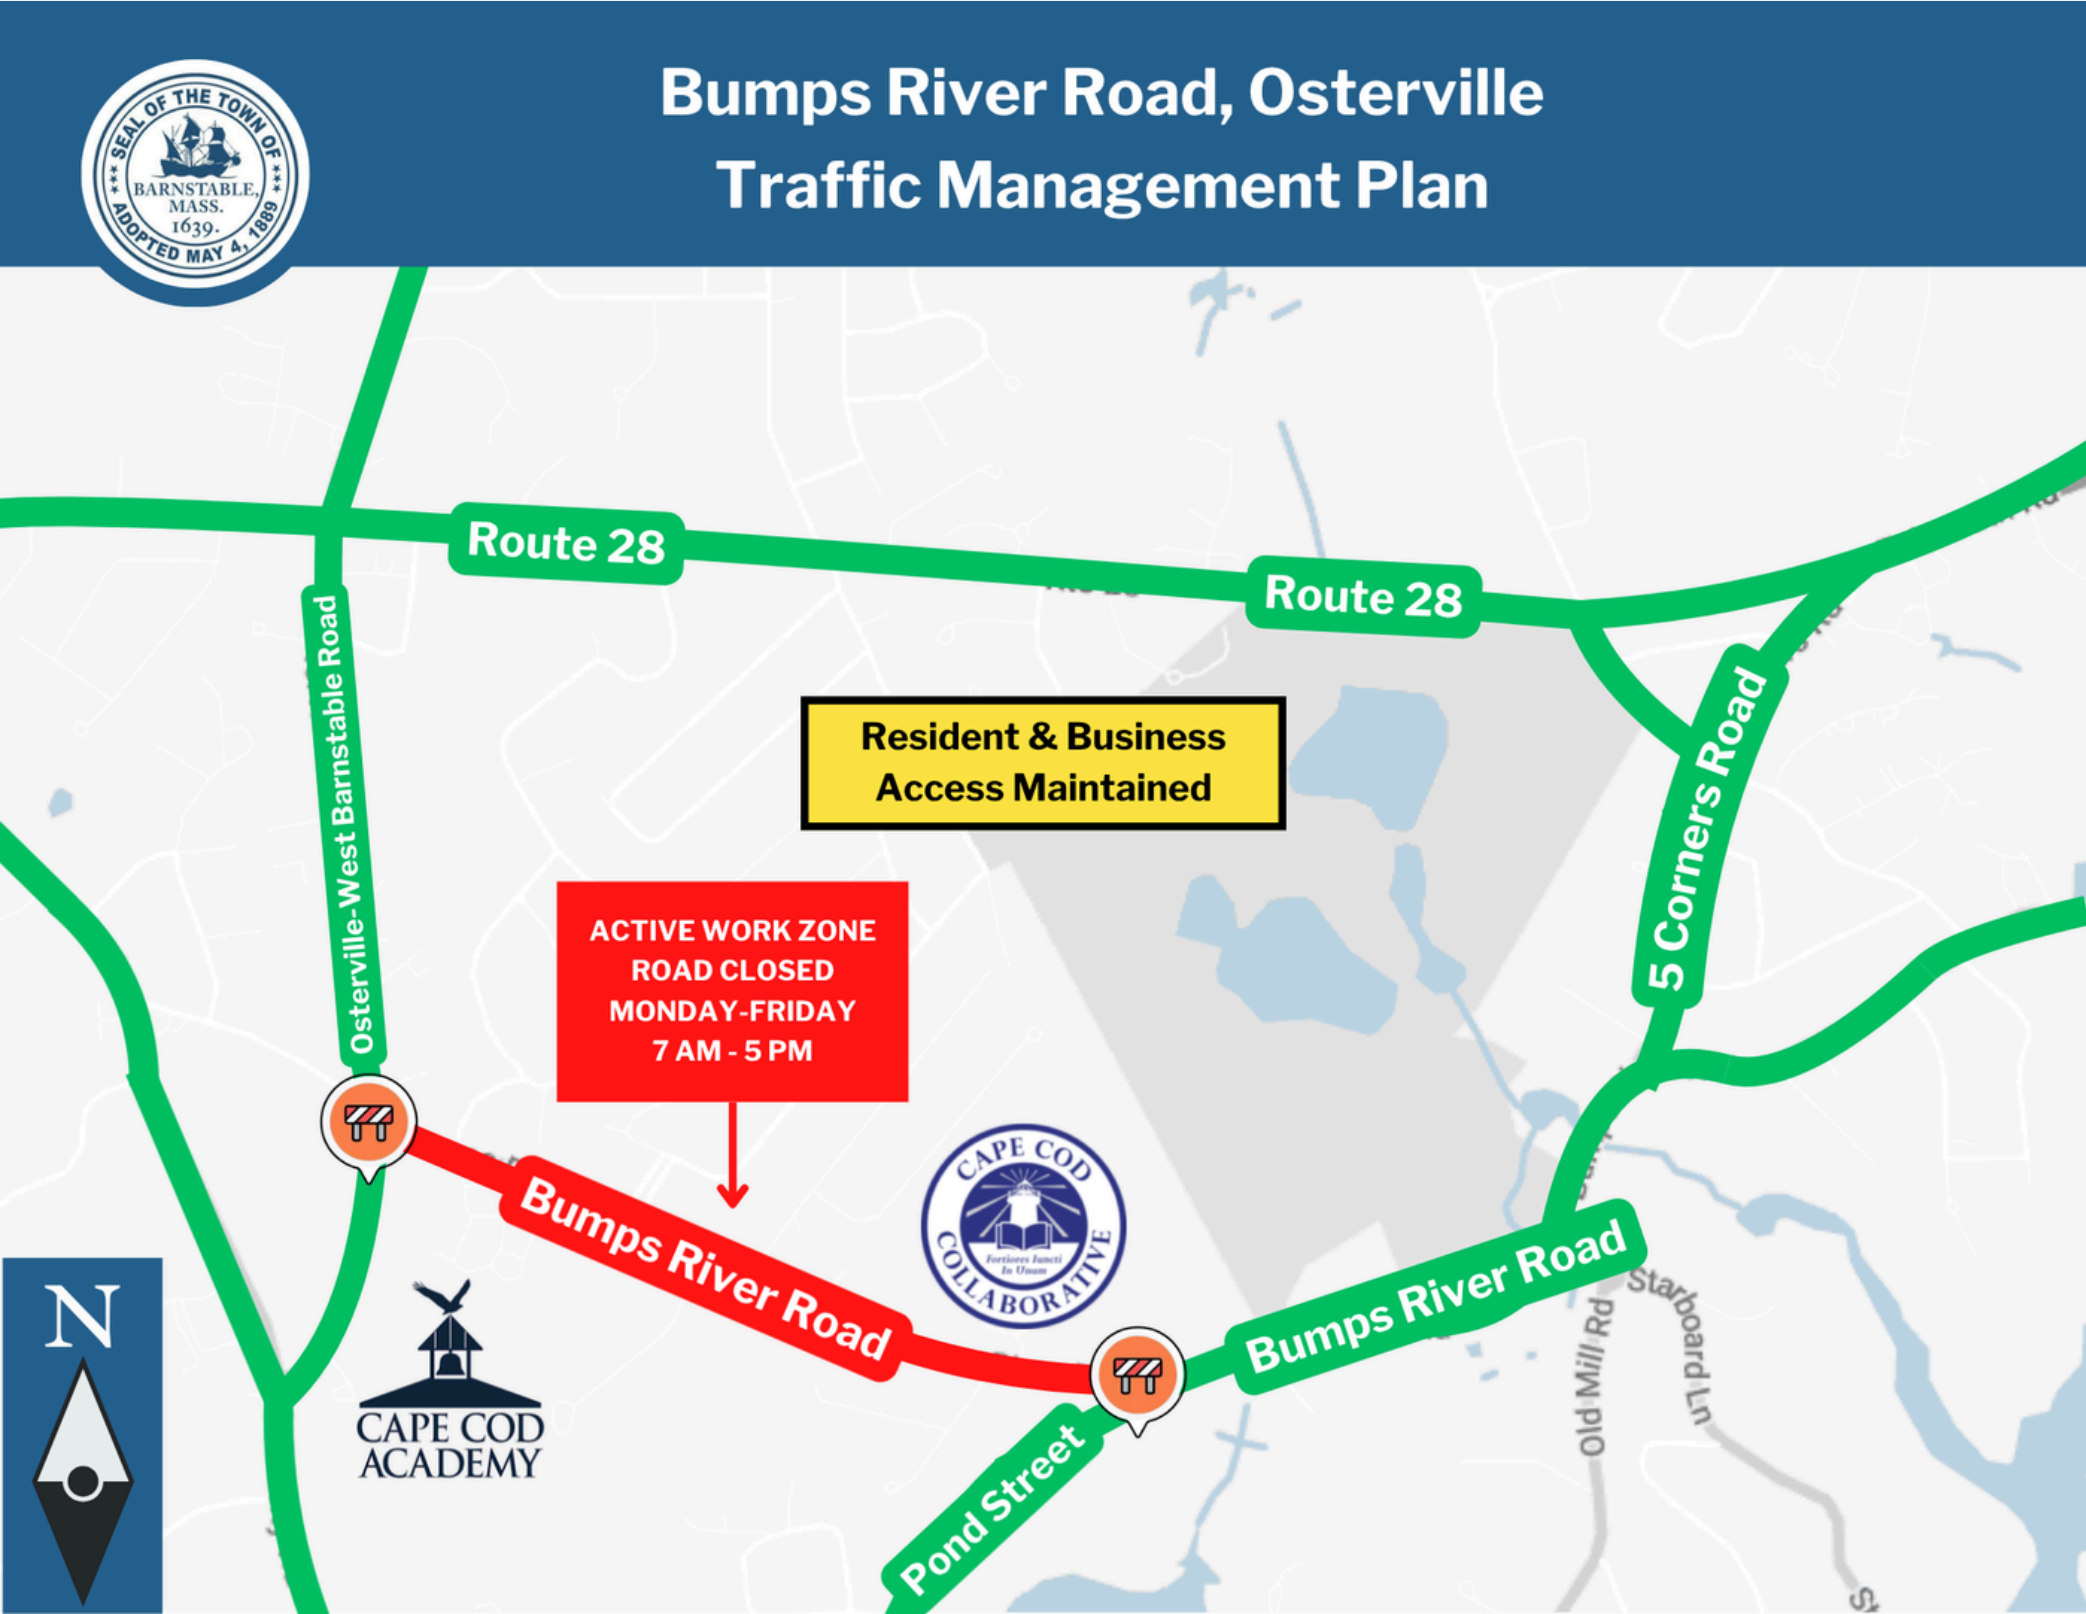


Route 28 West Sewer Expansion Project

Route 28 (OVERNIGHT) Traffic Mangement Plan

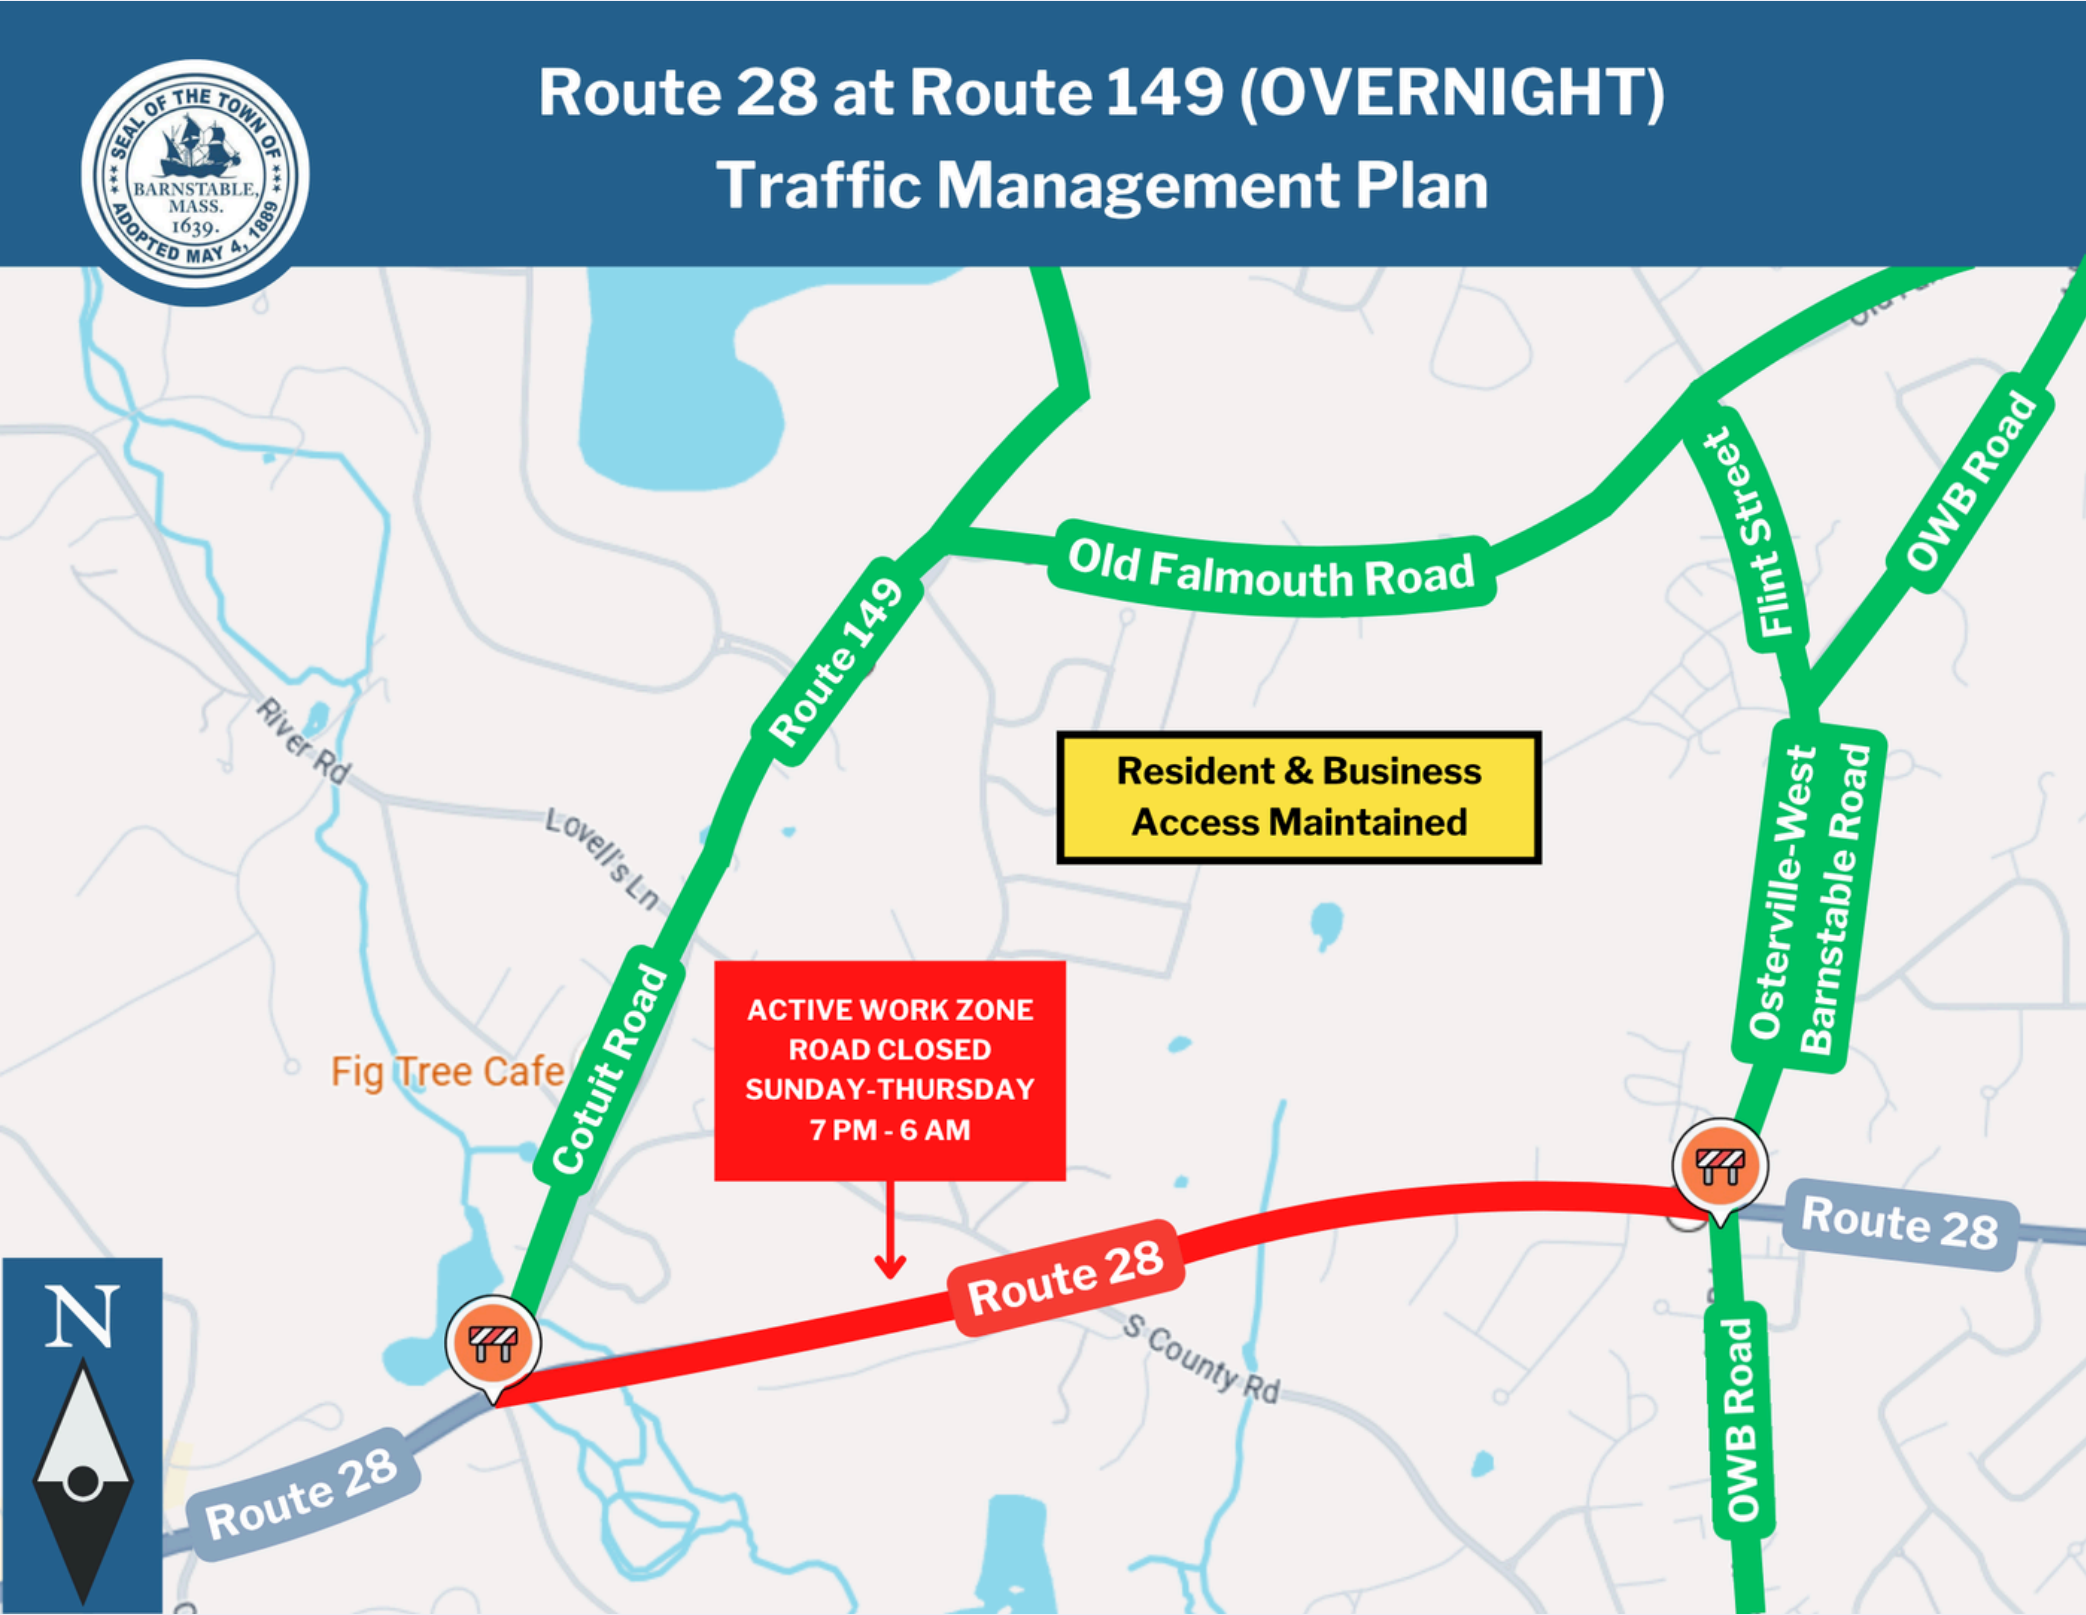

Centerville Village - North Sewer Expansion Project

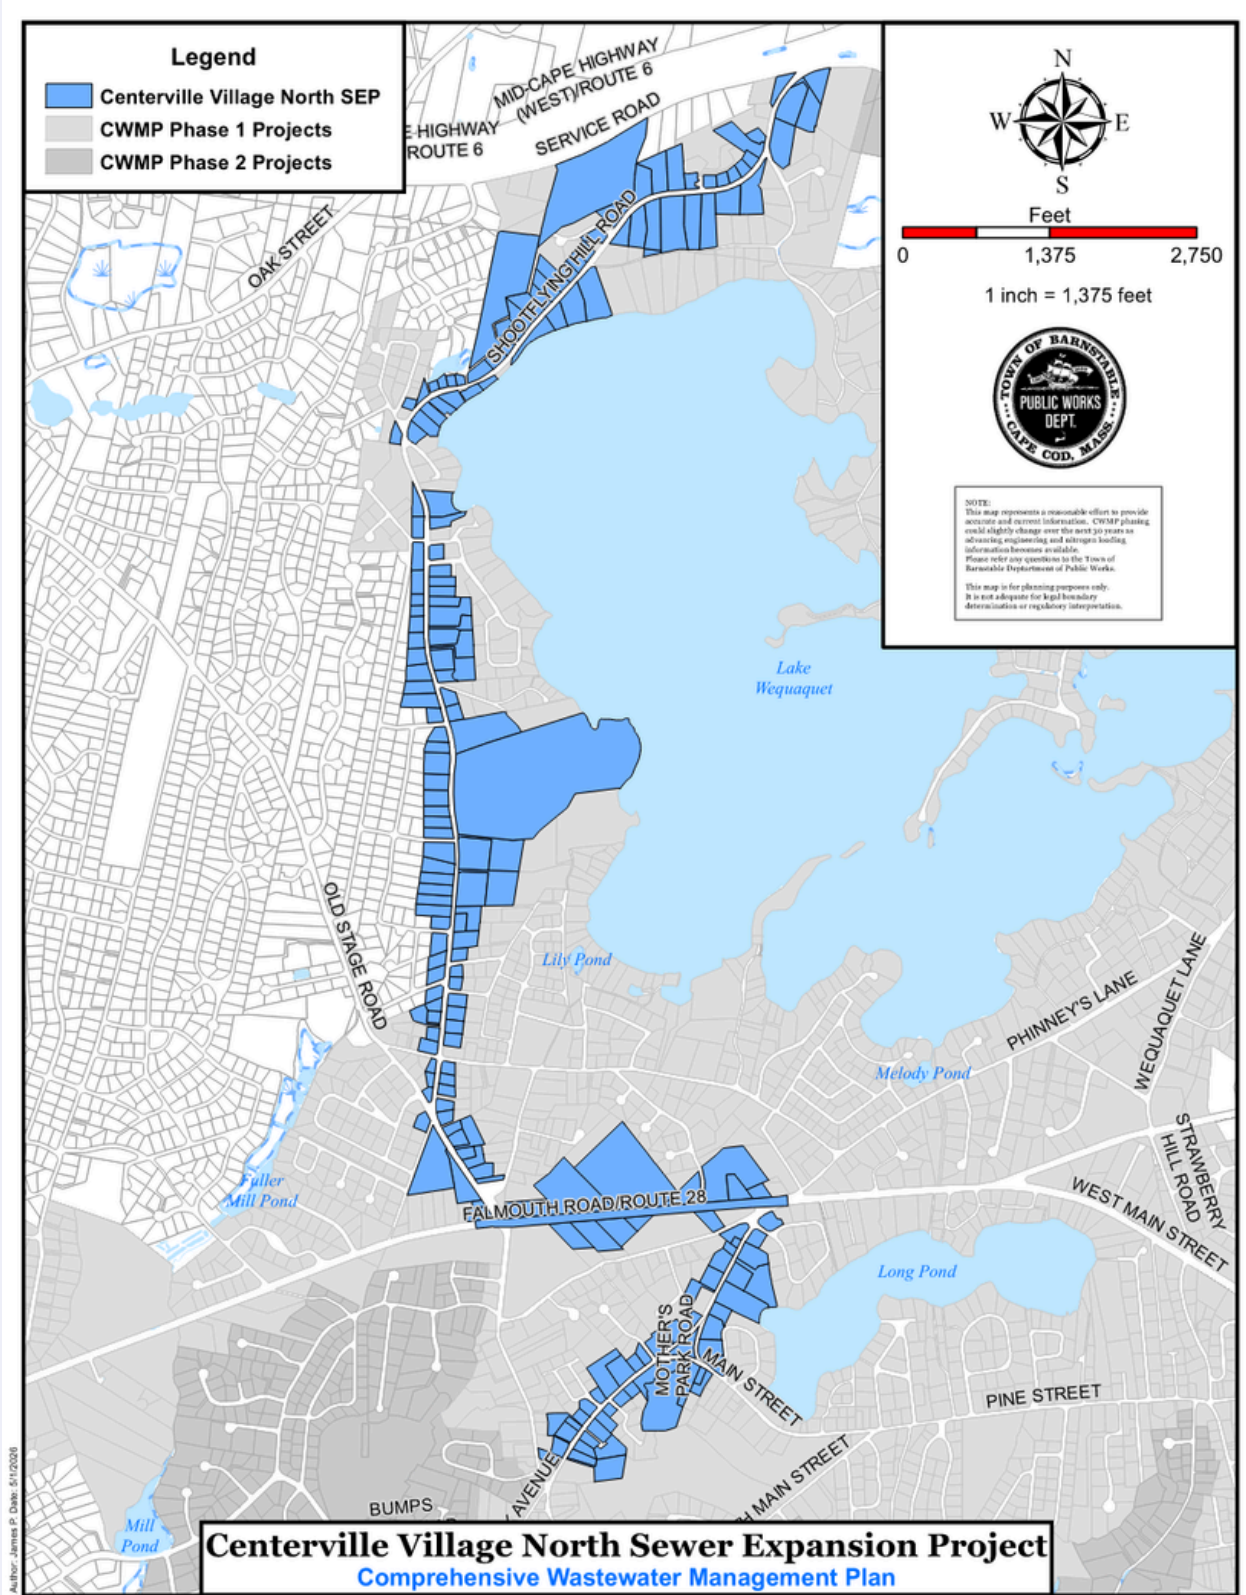

Fall 2026 Construction Season

Work Zone 1 – Main Street, Centerville / Mother’s Park

- **WHEN:** September 8
- **TIME:** Monday - Friday, 7:00 AM to 5:00 PM
- **WHERE:** Work will begin in the vicinity of Main Street, Centerville @ Mother’s Park and Phinney’s Lane and will advance south along Main Street to the intersection at Old Stage Road.
- **TRAFFIC IMPACT:** Portion of Phinney’s Lane and Main Street, from Pine Street to Old Stage Road, will be closed to thru traffic. Traffic management plans under review.

Work Zone 2 – Route 28 (OVERNIGHT)

- **WHEN:** September 14. (Requested to mobilize and stage on September 13, at 12:00 AM.)
- **TIME:** Overnight, Monday - Thursday evenings, from 7:00 PM to 6:00 AM
- **WHERE:** Work will begin within the vicinity 1661 Falmouth Road advancing toward the Old Stage Road intersection. Contractor will be working in and past the Old Stage intersection.
- **IMPACT:** Route 28, from Phinney’s Lane to Old Stage, will be closed to thru traffic; however businesses will remain accessible via posted detour and with assistance from onsite traffic control.


NOTE: Additional traffic modifications will be needed for the Old Stage Road intersection and will be communicated prior to that work commencing.




Centerville Village - North Sewer Expansion Project

Route 28 (OVERNIGHT) Traffic Mangement Plan

Sample Business Accessibility Map

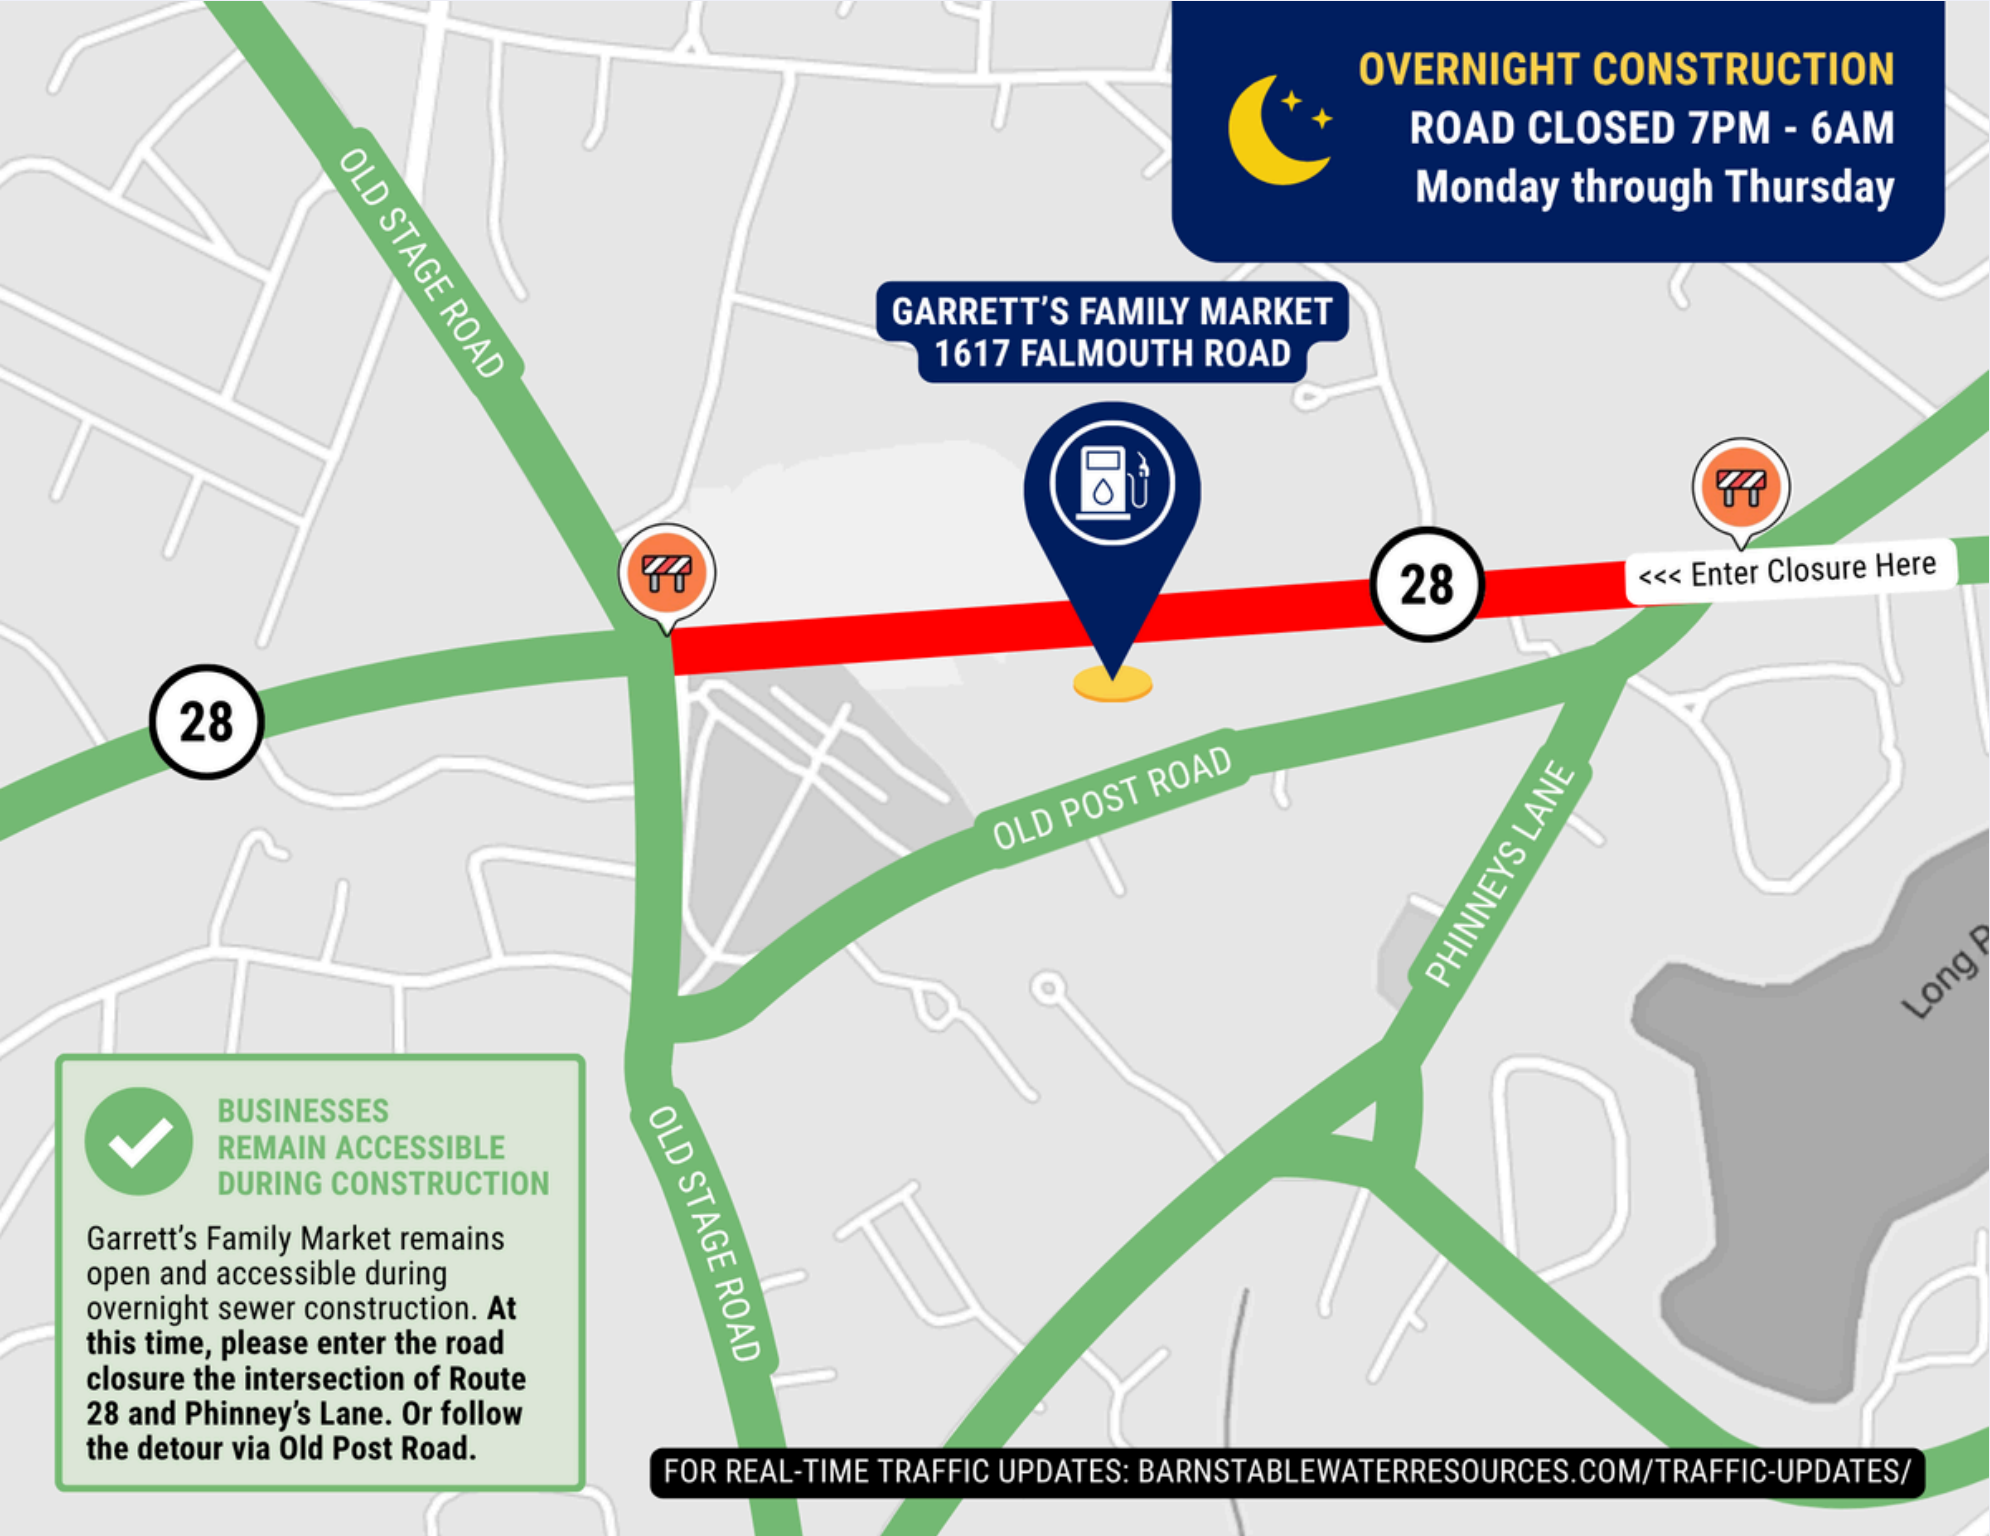

Phinney's Lane Neighborhoods Sewer Expansion Project

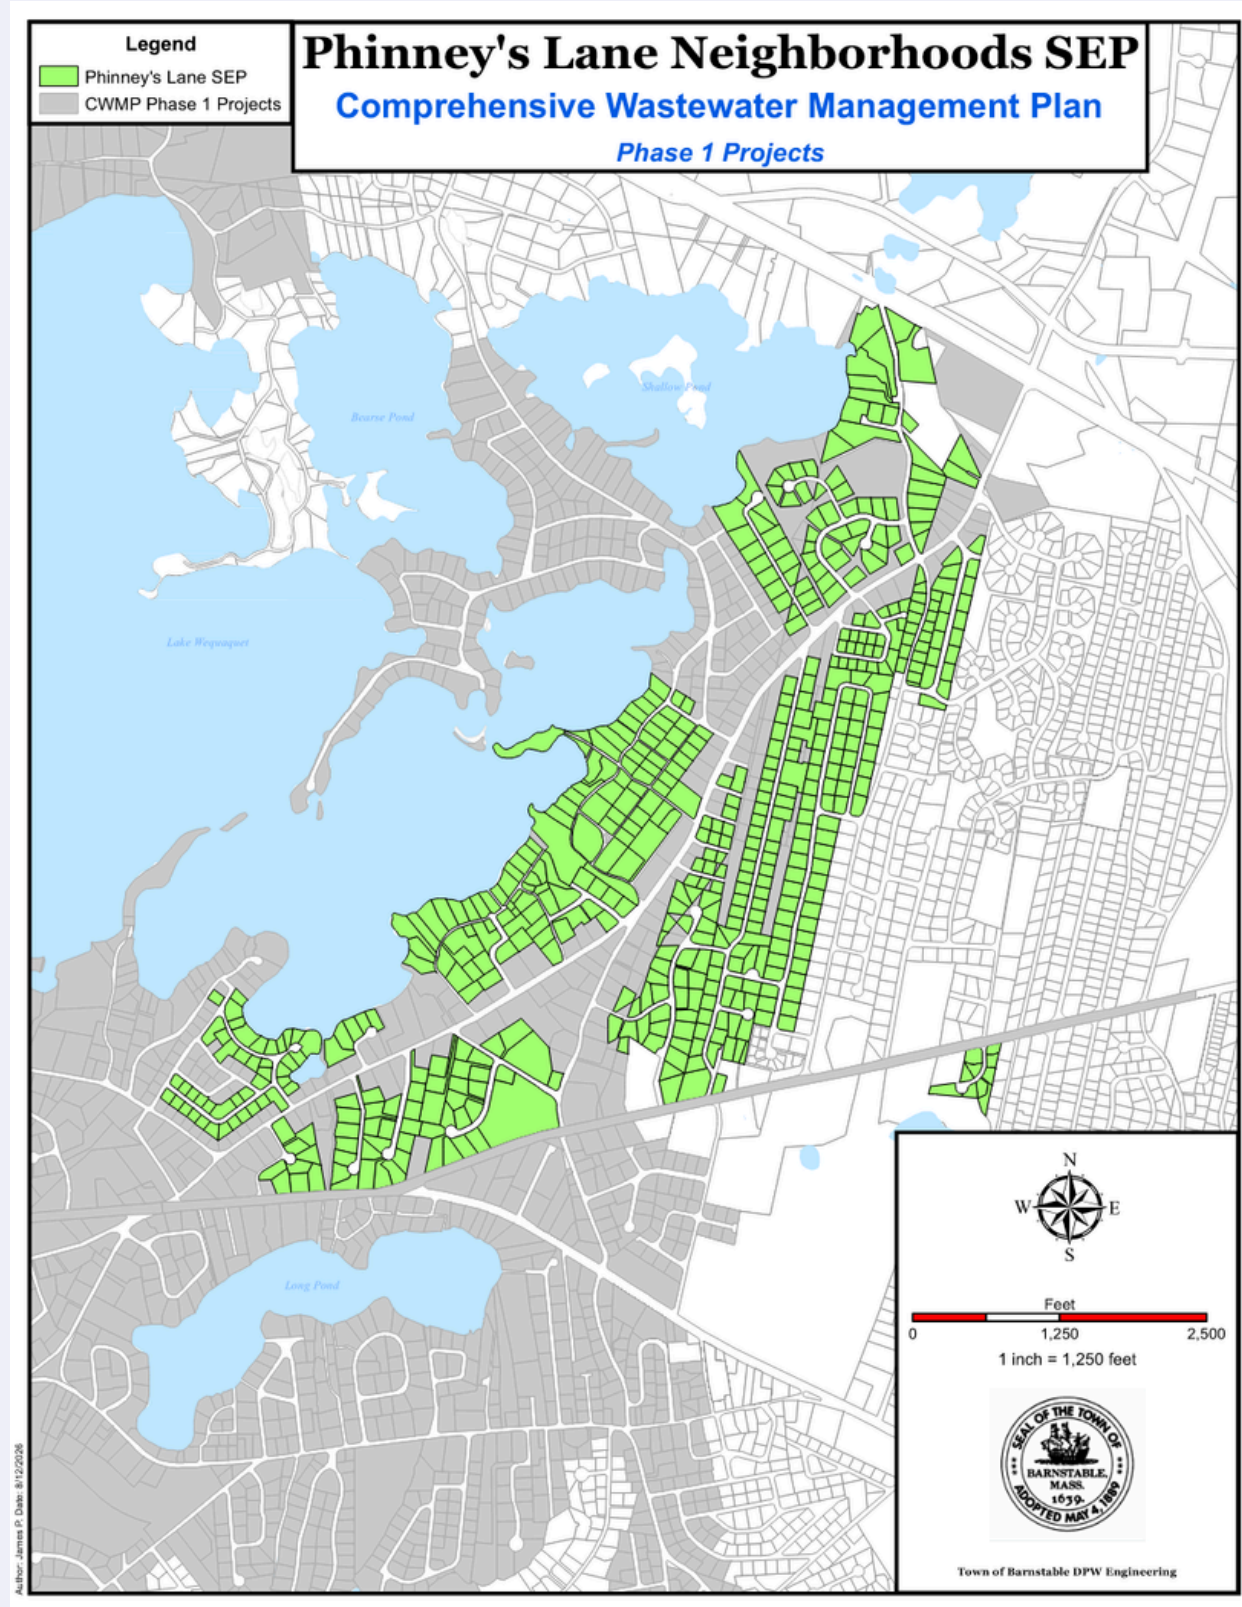

STATUS: Pre-Construction Planning

Contract Awarded to Robert B. Our Co., Inc.

Next Steps:


- Town and Contractor coordinating site walk and pre-construction meeting
- Contractor currently anticipates beginning construction in November
- Contractor has developed draft schedule, Town is reviewing

Communications and Outreach Efforts:

- Continuing to attend HOA annual meetings and brief neighborhoods upon request
- Preparing Formal Project Notification
 - Sent and tracked via Certified Mail
 - Includes Sewer Service Location Form
 - Includes resources for Spanish and Portuguese translations
- Coordinating next Public Informational Meeting
 - October 7th at 6:00 PM
 - Will be hosted at Barnstable High School, recorded, and available for future viewing
- Construction outreach will be performed neighborhood-by-neighborhood
 - 4-weeks out: mailed letter with construction schedule
 - 2-weeks out: pre-scheduled neighborhood meeting
 - 1-week out: door hanger with key access reminders



Centerville Village - South Sewer Expansion Project

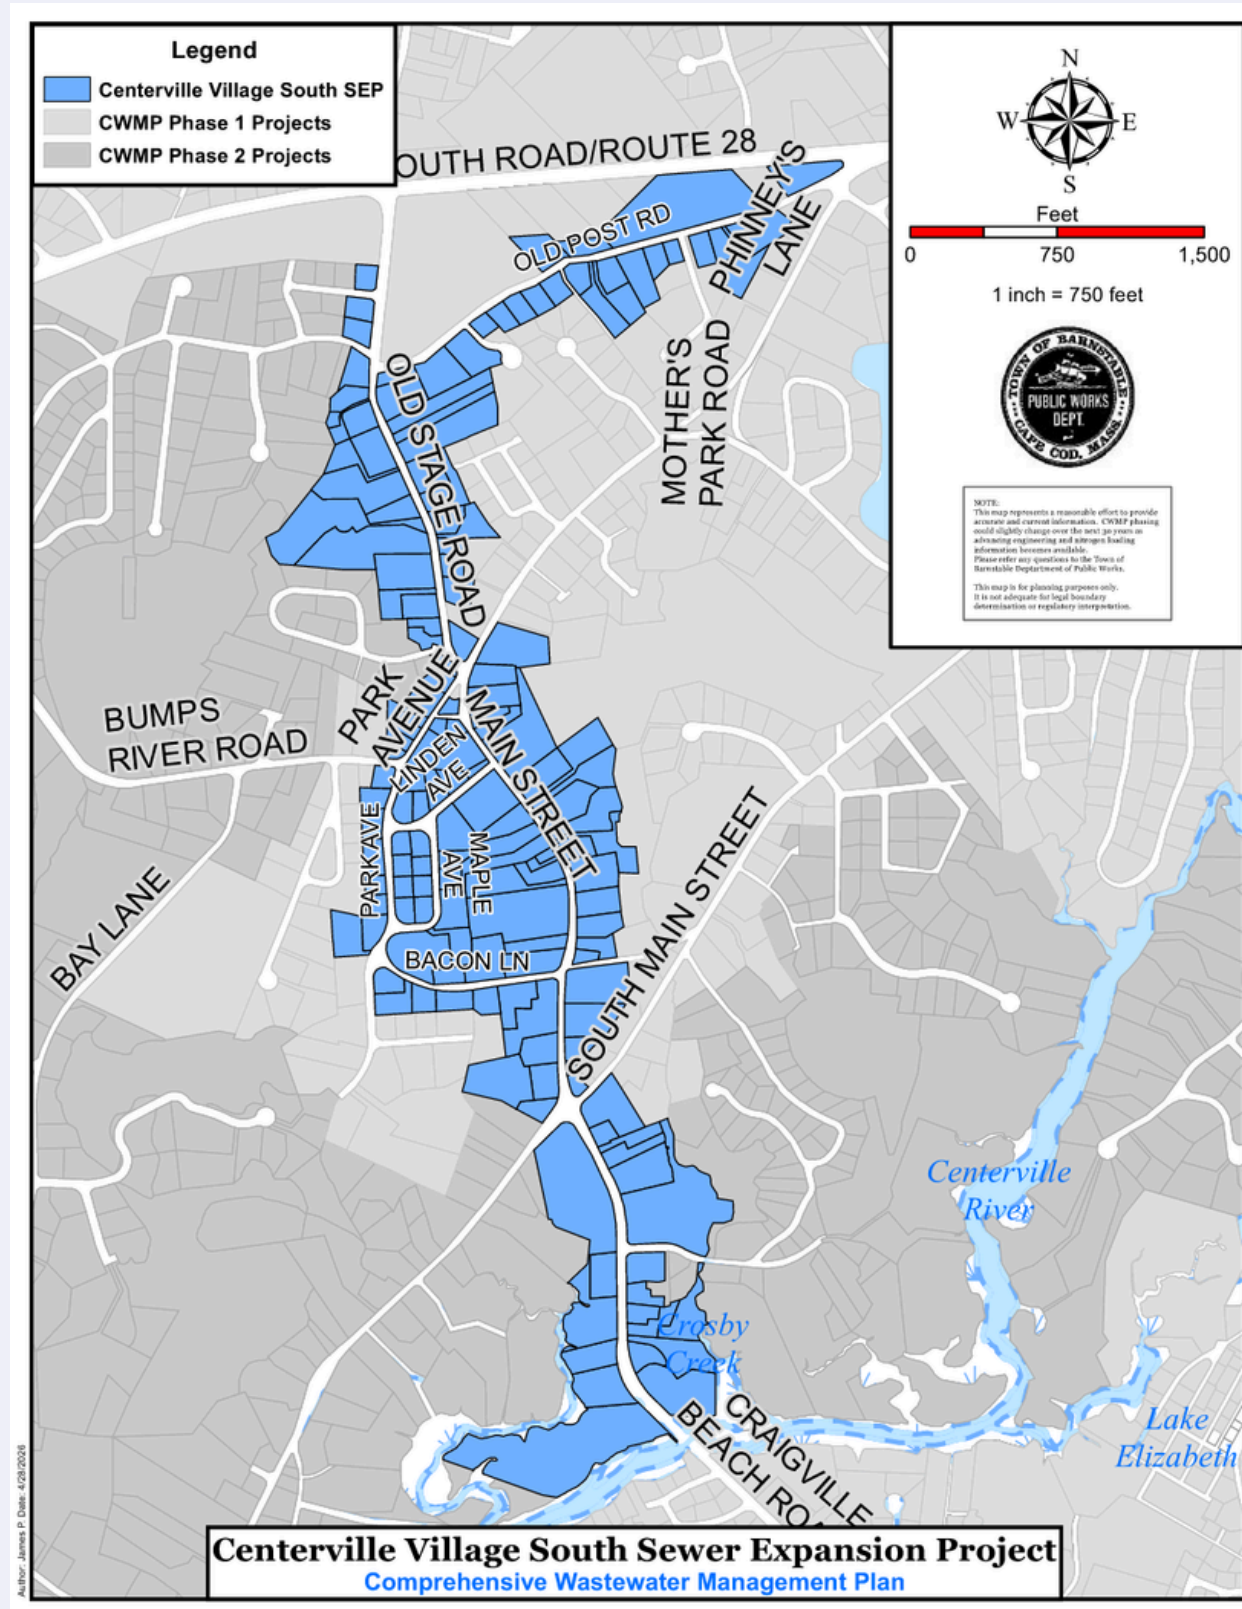

STATUS: Pre-Construction Planning
Contract Awarded to C. Naughton Corp.

Next Steps:

- Town and Contractor coordinating site walk and pre-construction meeting
- Contractor currently anticipates beginning construction in January 2027
- Contractor has developed draft schedule, Town is reviewing

Communications and Outreach Efforts:

- Providing regular briefings to Centerville Civic Association
- Preparing Formal Project Notification
 - Sent and tracked via USPS Certified Mail
 - Includes Sewer Service Location Form
 - Includes resources for Spanish and Portuguese translations
- Coordinating next Public Informational Meeting, to occur prior to construction commencing



Upcoming Sewer Expansion Projects

Long Pond Area Sewer Expansion Project

STATUS: Design advancing to 90%

- Vote anticipated at this week's Town Council meeting related to the taking of roadway utility easements on private roads identified within the project (Agenda Item 2027-011)
- Letter mailed to all property owners

Great Marsh/Shootflying Hill Roads Neighborhoods Sewer Expansion Project & Huckins Neck Area Sewer Expansion Project

STATUS: Survey and preliminary design ongoing

- Survey work will continue throughout the summer
- Utility markouts and soil borings anticipated to begin in September
- Letter mailed to all property owners

Prince Cove Sewer Expansion Project

STATUS: Design contract awarded to Tighe & Bond

- Contract with Procurement for execution
- Coordinating kick-off meeting





BARNSTABLE
Water Resources
