

Centerville Playground and Parking Lot Project

Project Briefing Status: Construction Documents

April 2024



Centerville Playground Advisory Group

John Gleason - Director of Recreation

Chris Gonnella - Director of Community Services Department

Patti Machado - Former Recreation Director/advocate for all things related to our youth

Mark Marinaccio - Town Architect, DPW

Judy Reale - Playground Consultant

Molly Sproul - Playground abutter and devoted resident

Richard Ventrone - Lead Architect, DPW

Current Town Council Vice President Craig Tamash attended last informational session

Former Advisory Group members:

Nikolas Atsalis, Precinct 4 - Former Town Councilor

Madeline Noonan - Former Director of Community Services Department

James Tenaglia - Former Recreation Commission Member & Liaison to CPC

Nancy White - Playground Consultant (deceased)

Public Meetings were held on January 31, 2023 and November 11, 2023.

Hazardous Conditions Observed

- Due to observed hazardous conditions the Centerville Playground will remain closed
 - Equipment disassembly and removal anticipated over the coming weeks/months








Hazardous Conditions Observed

- Failed retaining wall at front parking
- Failed structural elements at wood structure
- Broken play equipment
- Exposed foundations
- Deteriorated wood steps
- Insufficient surfacing

Existing Site Conditions

- Aged, failing playground equipment
- No accessible path to playground
- Failing retaining wall
- Deteriorated landscape ties
- Aged neighborhood ballfield facility

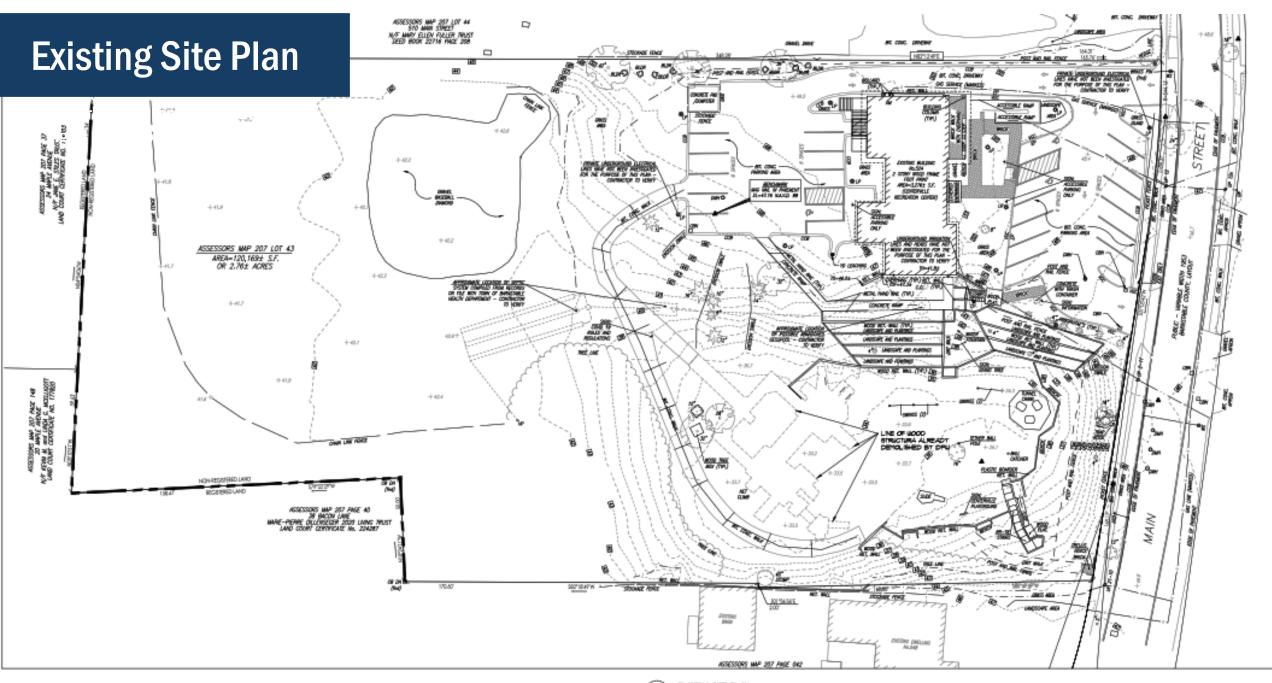



Project Status

- Project is currently in the Construction Document phase
- Project consists of multiple components
 - Retaining wall construction (funded)
 - Playground and accessible parking lot (funded)
 - Ballfield (pending CPA approval)
- Construction of the retaining wall, playground, and parking lot anticipated to begin Fall 2024 with estimated completion Summer 2025

Proposed Site Plan


- Revise parking at a lower grade
 - 10 additional parking spaces
- Playground area fill
 - New accessible path to playground
 - Replace failed retaining wall
- Update ballfield
 - Regulation grass infield
 - Short outfield



Community Feedback & Interests

- Accessible path
- Accessible playground equipment
 - Swings
 - We-go-round
 - Treehouse
 - Ship play structure
 - Crab trap
 - Seesaw
 - Surfboard
 - Shipwreck
 - Sea Lion


- Shaded seating
- Poured in place and artificial turf surface
- Water bottle filling station

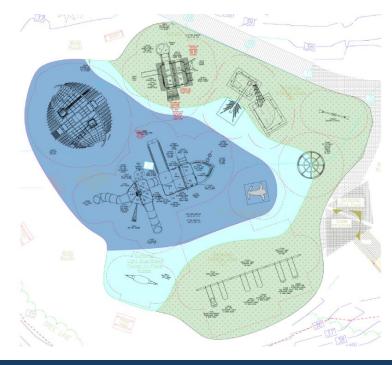

Playground Equipment

- Swings
- We-go-round
- Tree house
- Ship play structure
- Crab trap
- Seesaw
- Surfboard



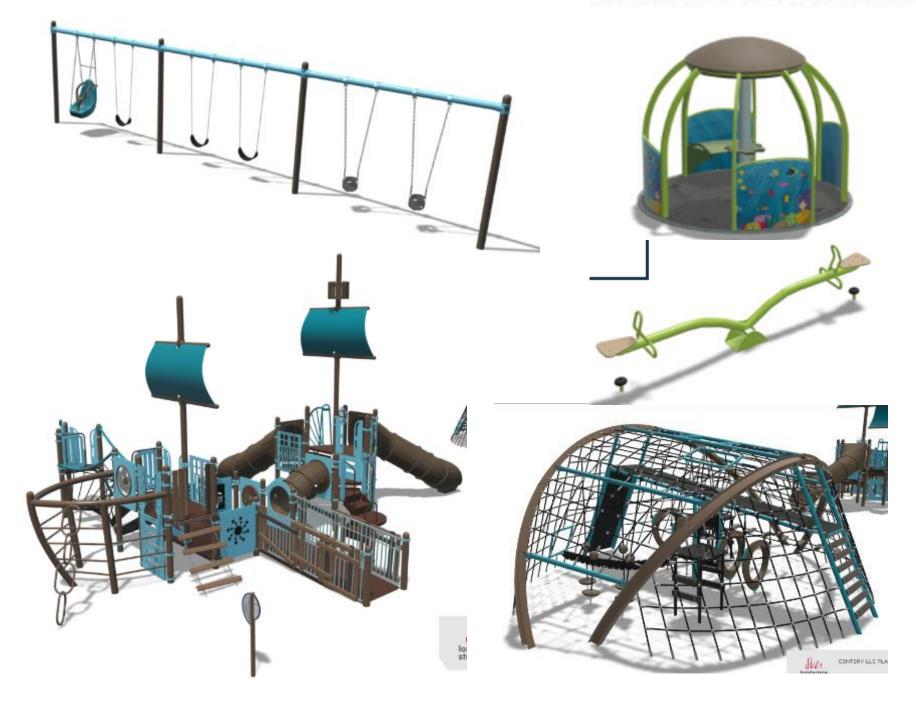

Playground Equipment Alternate - 1

- Shipwreck Sea Lion













MEO24339 • 3.26.2024 ELEMENTS FOR A GREAT OUTDOORS






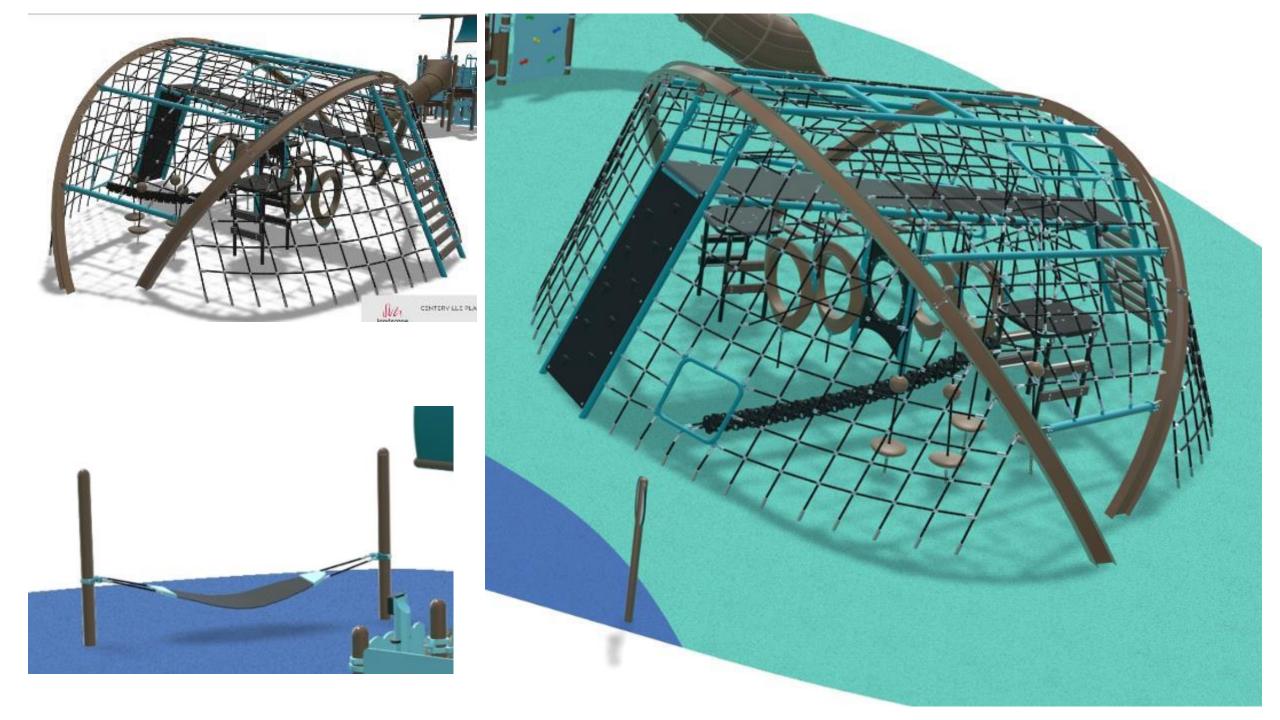






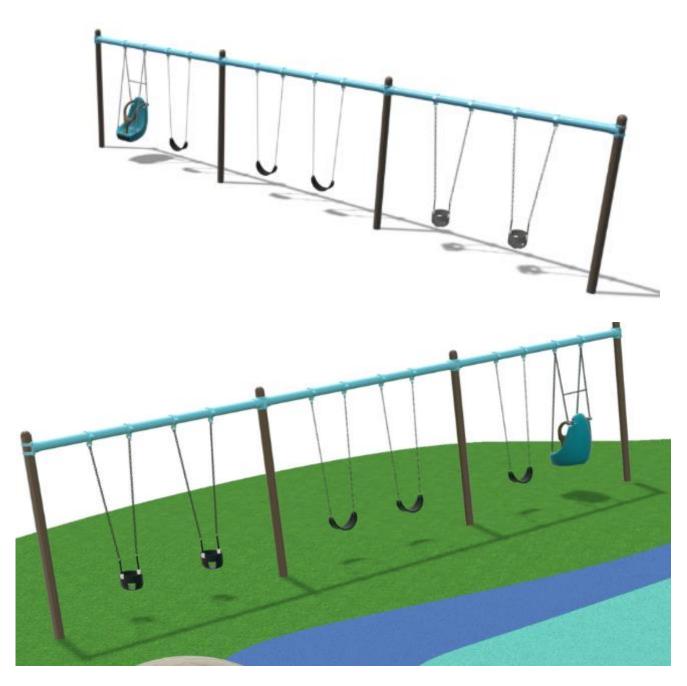



Field Evaluation

- Currently is not a regulation Little League field
- Currently used for:
 - Junior Cape League
 - Barnstable Little League practices and games
 - Small pick-up wiffle ball, softball, and baseball games
- Included in Comprehensive Field Study
 - At that time, a grass multi-use field was recommended
- Funding is pending
 - A Community Preservation Act (CPA) funding request has been made

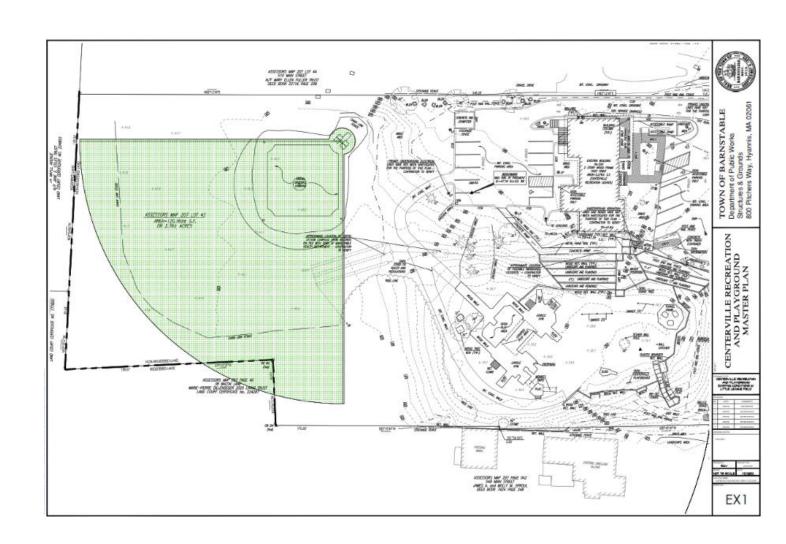

Community Feedback & Interests

- Little League Regulation Infield
- Short Outfield 150 Ft
- Accessible
- Level out the field
- Grass infield and outfield
- New backstop
- Neighborhood pickup games
- Little League practice



Centerville Playground Anticipated Schedule

Community Outreach Meeting	1 day?	Tue 11/21/23	Tue 11/21/23	1/21	11/21									
Playground Design & Advisory Group Meetings	90 days	Wed 11/22/23	Tue 3/26/24	1/22		3/26								
					0/40								<u> </u>	-
Community Preservation - Field Funding - Original Request 8/31/23	90 days	Mon 3/18/24	Fri 7/19/24		3/18		7/1	9					-	-
CPC First Read	1 day?	Mon 3/18/24	Mon 3/18/24	_	3/18									
Community Preservation - Full Application	1 day?	Mon 4/22/24	Mon 4/22/24		4/22	4/22	_							
Town Council - Field Funding Approval	90 days	Mon 7/22/24	Fri 11/22/24			7/22	_		11/22					
Field Design	90 days	Mon 11/25/24	Fri 3/28/25	_		i		11/25	-	3/2	28			
Field Bid	45 days	Mon 3/31/25	Fri 5/30/25			1			3/	31	5/3			
Field Contract Negotiation	21 days	Mon 6/2/25	Mon 6/30/25	_							= 6	6/30		
Field Construction	120 days	Tue 7/1/25	Mon 12/15/25					-		7	7/1		-	12/15
Retaining Wall Design Contract	30 days	Tue 3/12/24	Mon 4/22/24	-	3/12	4/22								
Retaining Wall Construction Documents	90 days		Mon 8/26/24		4/2	3		8/26					\pm	
Retaining Wall Bid	45 days	Tue 8/27/24	Mon 10/28/24	-		8	/27		10/28				1	
Retaining Wall Contract Negotiation	14 days		Fri 11/15/24	-			10	/29 🇯	ղ 11/15					
Retaining Wall Construction		Mon 11/18/24	Fri 3/21/25				1	1/18		3/2	1		\dotplus	
					2/5		7/1	9					-	
Playground, Parking Construction Documents	120 days		Fri 7/19/24	_ —	4/15	-	7/5						+	_
Engineering Storm Water Design	60 days	Mon 4/15/24	Fri 7/5/24	1/1		4/5		-		+ +			+	+
Playground Equipment Order	60 days	Mon 1/15/24	Fri 4/5/24	1/10		7/22		9/2	0	+ +		-	+-	+
Playground, Parking Bid	45 days	Mon 7/22/24	Fri 9/20/24	_		1122	9/23		10/21	+ + +			$\dot{+}$	-
Playground, Parking Contract Negotiation	21 days	Mon 9/23/24	Mon 10/21/24	_	+		100		10/21	+ +		8/11	+-	+
Playground, Parking Construction	210 days	Tue 10/22/24	Mon 8/11/25				100					- Prili	+-	-

Budget

- Playground and Parking Lot
 - \$816,793 for Playground Renovations
 - FY22 Approved Community Preservation Act (CPA) funds
 - \$827,376 for Parking Lot and Access Improvements
 - FY23 Approved Capital Improvement Project (CIP) funds
- Field
 - Currently estimated at \$468,000
 - Requesting funds via CPA/CIP for field construction

Questions?
